

APPENDIX A

BORE AND DRILL LOG RECORD SHEETS

LOCATION OF BOREHOLES

Borehole No.	Co-Ordinates		Reduced Level		Date	
	N(m)	E(m)	Top	Bottom	Start	Finish
Over Water:-						
D1	257365	324804	-7.0	-57.32	30.3.76	8.4.76
D2	257419	324851	-8.0	-50.60	9.3.76	24.3.76
D3	257307	324754	-5.7	-40.14	21.4.76	11.5.76
D4	257780	325160	-8.0	-30.33	2.6.76	8.6.76
D5	257661	325060	-14.0	-43.85	24.5.76	28.5.76
D6	257481	324904	-6.8	-43.23	17.5.76	20.5.76
D7	257389	324825	-8.0	-52.69	10.6.76	15.6.76
D8	257375	324813	-8.0	-51.54	16.6.76	18.6.76
D9	257369	324813	-8.0	-54.28	21.6.76	6.7.76
D10	257293	324744	-2.0	-25.66	8.7.76	27.7.76
D11	257305	324753	-6.0	-29.84	2.8.76	4.8.76

East Abutment:-

E1	257985	325347	+6.99	-8.20	27.7.76	6.8.76
E2	257996	325334	+7.42	-7.18	6.8.76	18.8.76

West Abutment:-

W1	257257	324712	+12.07	+0.00	27.4.76	5.5.76
W2	257246	324702	+17.35	-2.92	18.8.76	31.8.76

West Approach Cutting:-

WA1	257171	324638	+33.80	+16.44	6.5.76	25.5.76
WA2	257086	324564	+29.78	+14.53	26.5.76	8.6.76
WA3	257014	324473	+24.78	+13.51	10.6.76	21.6.76

Boreholes Over Water for Feasibility Studies:-


X J1	257206	324925	-7.5	-48.08	May 1975
J3	257605	324882	-8.8	-42.17	Sept. 1975
J4	257349	324750	-6.3	-48.60	Sept. 1975

No. 1 Six Boreholes put down in August to October, 1963,
to approximate locations shown on Drawing No. 2,
No. 6 Results reported by I. B. Jennings, 1964.

Note: Holes J1, J3 and J4 were previously
No. BH1, BH3, and BH4 respectively.

SEISMIC SPREADS (APPROXIMATE LOCATIONS ONLY)
 — (1) TO (22) DEPARTMENT OF MINES REPORT 1975 / 32
 — 1 TO 11 DEPARTMENT OF MINES REPORT 1975 / 39

BOREHOLES - PHASE 1 SITE
 ⊗ D1 TO D11 ON ALL WEST WEST
 W1, W2 & E1, E2 WEST
 WA1 TO WA3 WEST
 BOREHOLES - PRIOR TO PHASE 1
 ⊗ J1, J2, J4 FEASIBILITY AFTER
 N° 1 TO N° 6

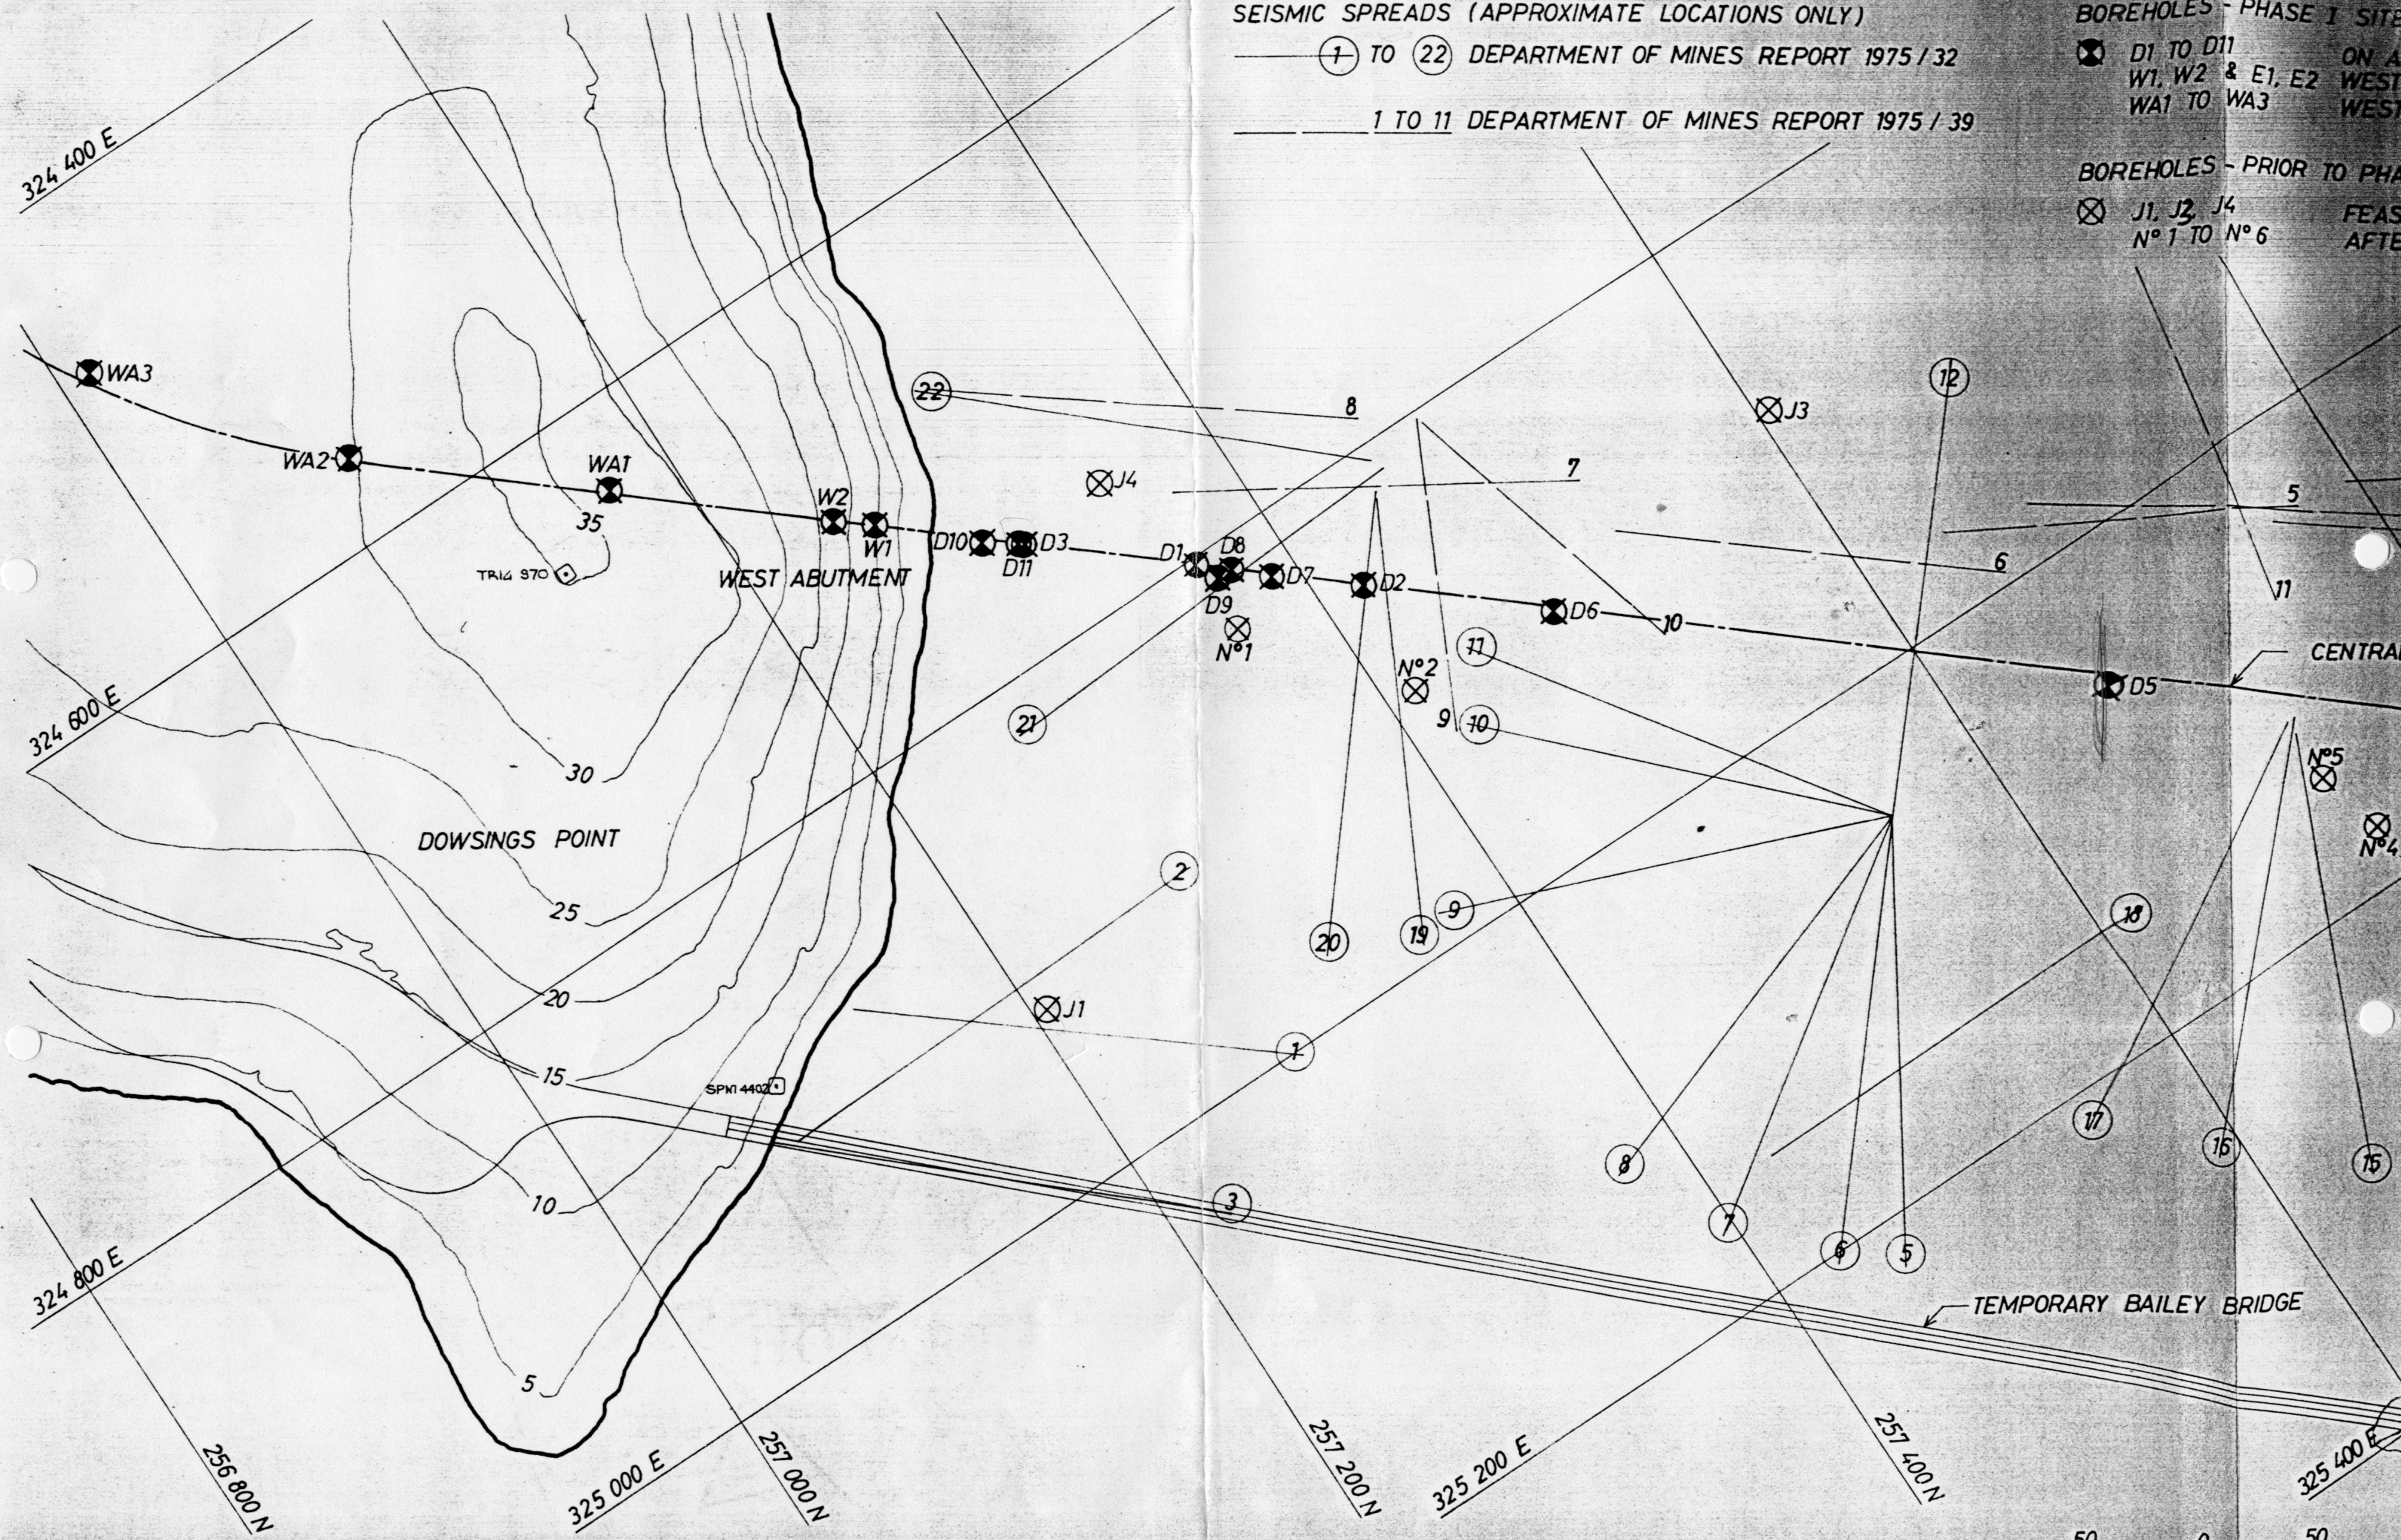

21 244



SEISMIC SPREADS (APPROXIMATE LOCATIONS ONLY)

① TO ②② DEPARTMENT OF MINES REPORT 1975 / 32


① TO ①① DEPARTMENT OF MINES REPORT 1975 / 39

BOREHOLES - PHASE I SITE INVESTIGATION

⊗ D1 TO D11 ON ALIGNMENT OVER WATER
W1, W2 & E1, E2 WEST / EAST ABUTMENTS
WA1 TO WA3 WEST APPROACH CUTTING

BOREHOLES - PRIOR TO PHASE I

⊗ J1, J2, J4 FEASIBILITY INVESTIGATIONS 1975
N° 1 TO N° 6 AFTER I.B. JENNINGS 1963 (APPROX. ONLY)

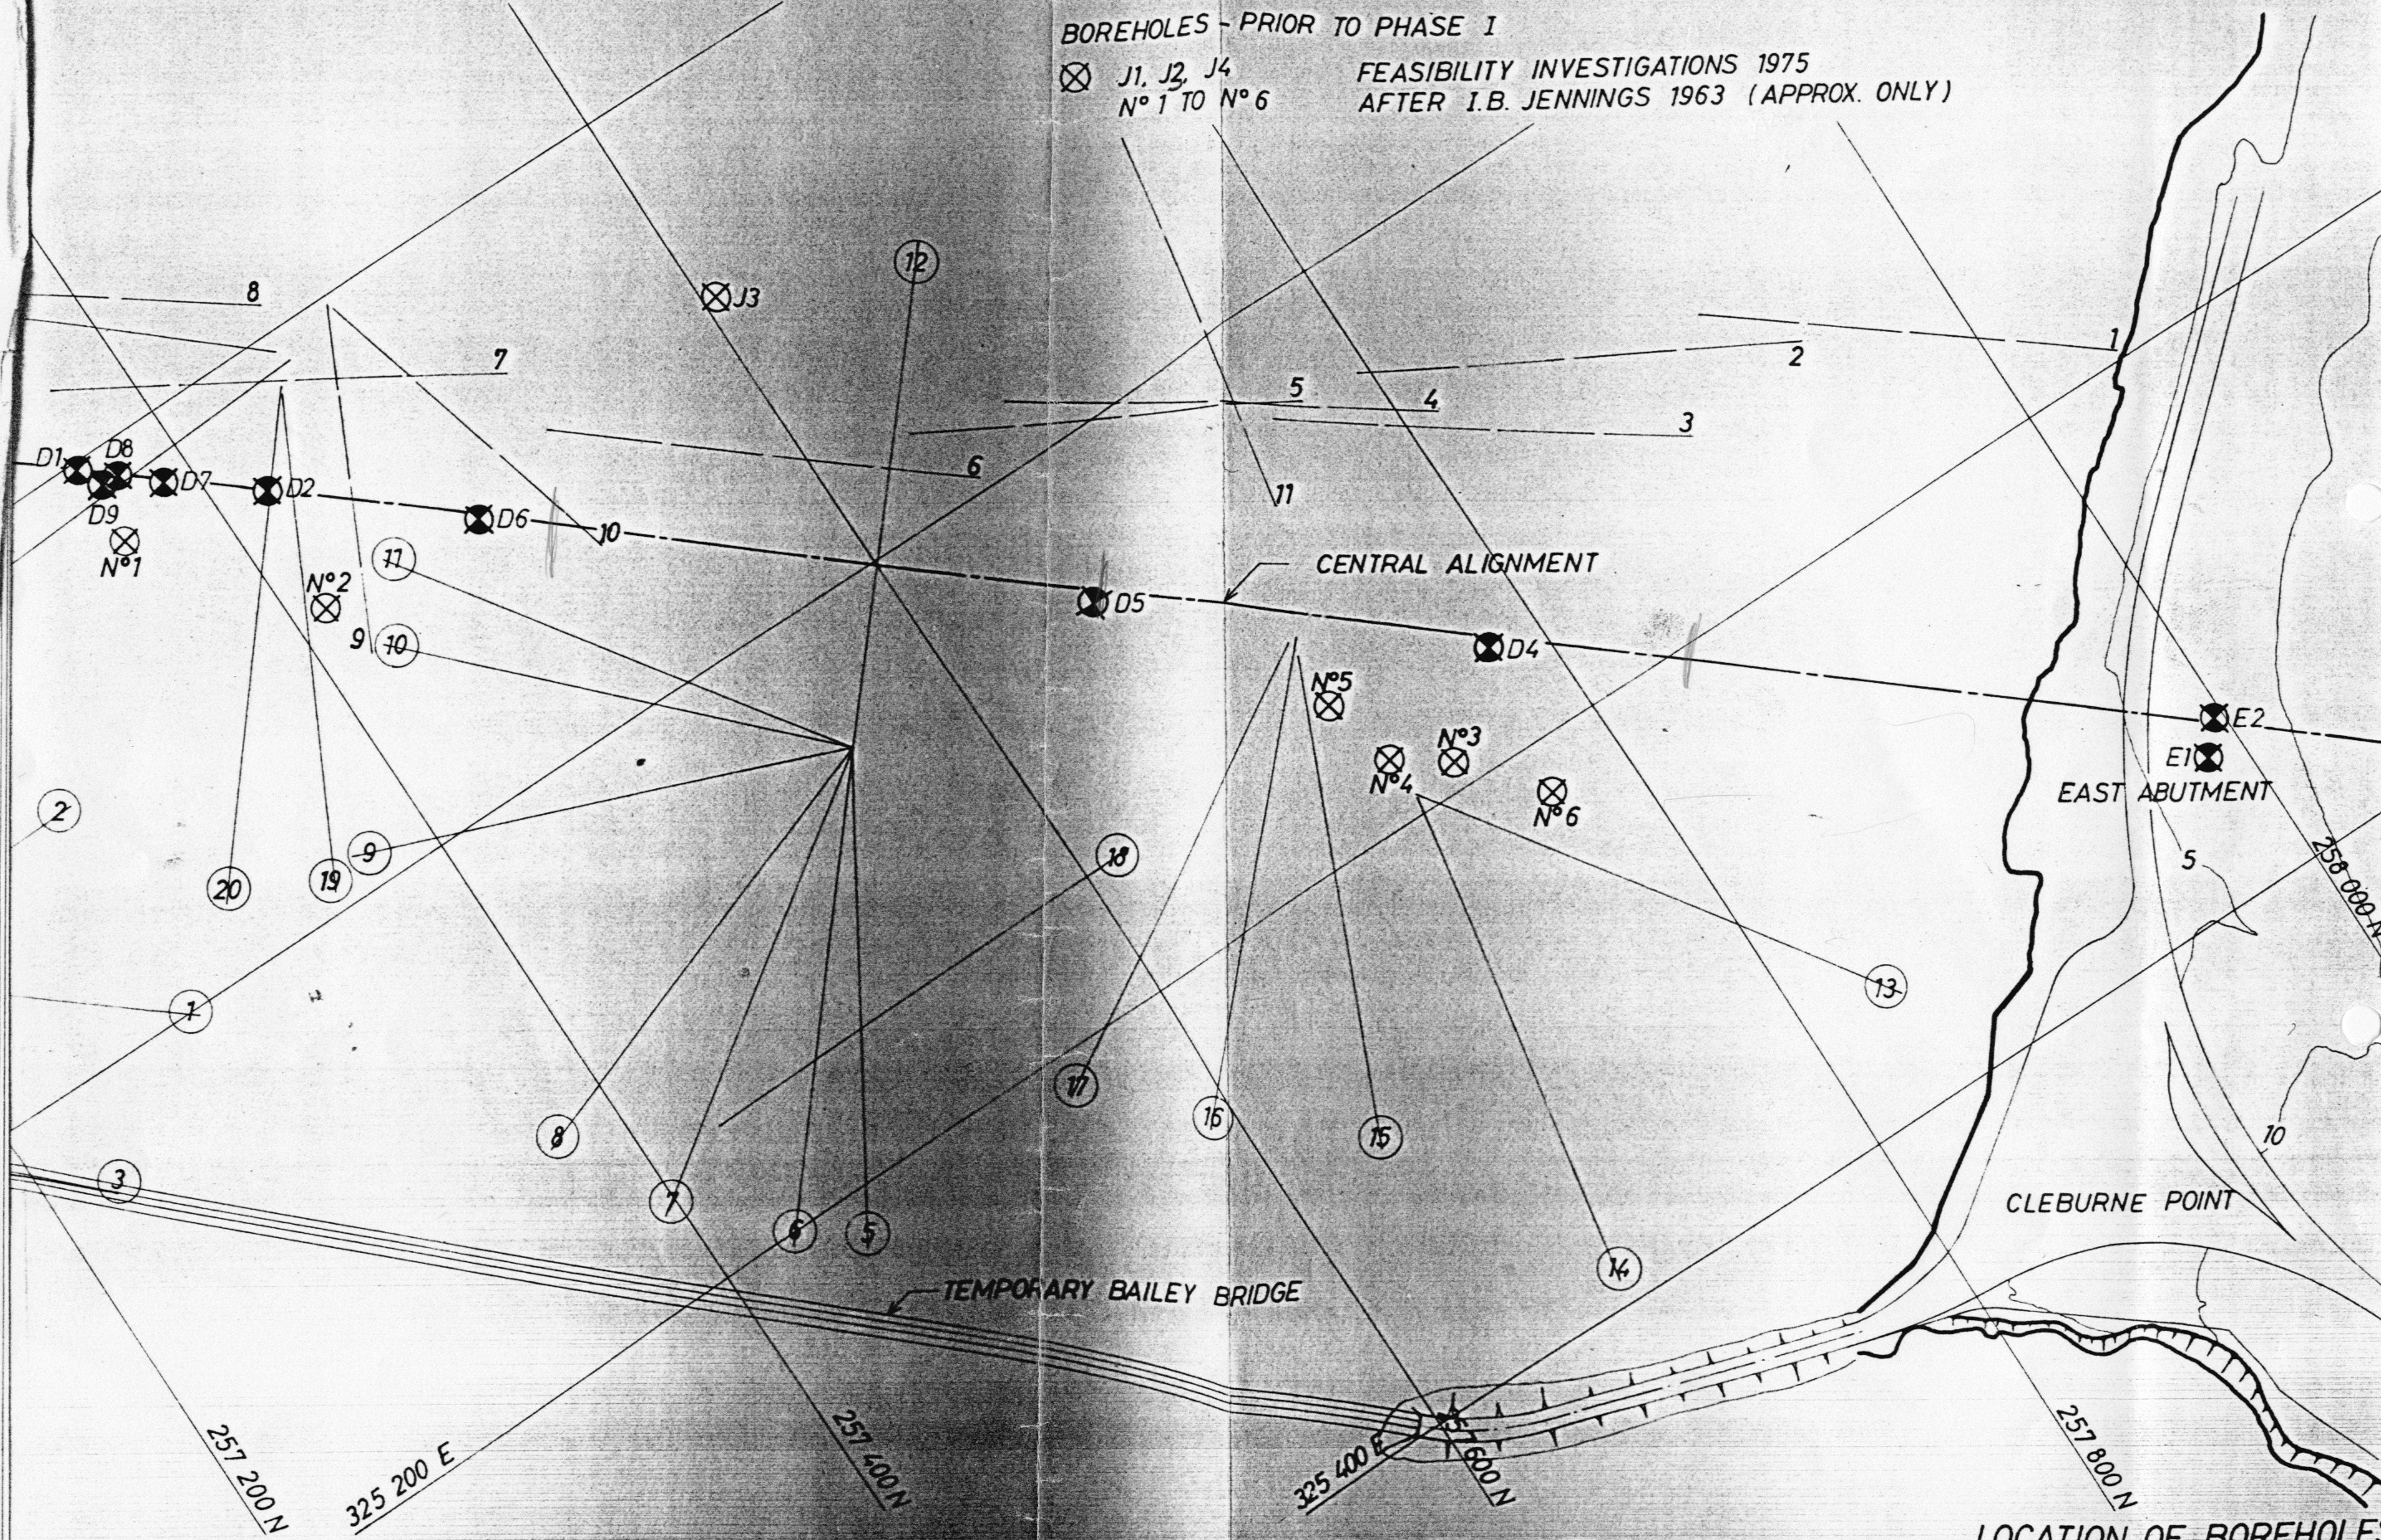

LOCATION OF BOREHOLES AND SEISMIC SPREADS
SECOND HOBART BRIDGE

mania

iage

ation

76

Ltd
neers

21 245



REF No 18312
 DEPARTMENT OF PUBLIC WORKS TASMANIA
 MATERIALS AND RESEARCH DIVISION

ACC 2
 PUR 0


QUAD 82 MAP SHEET 83122

BORE LOG RECORD

PROJECT		SECOND HOBART CROSSING PHASE 1 - SITE INVESTIGATION		BORE No.	D 3
Bore co-ordinates:		324754E 257307N E=524760N=5258950		FILE No.	01.0500
Surface R.L.:	0.00	Datum: State		Sheet no. 1	of 3
Angle from horizontal:	90°	Direction: -			
Rig type:	Meyhew 1000	Drill size:	6" Casing	Commenced:	21-4-76
Drilling by:	Mines Dept.	Water level:	River	Completed:	11-5-76
				Logged:	T.S.
				Checked:	W.K.

R.L.	Depth	Sample Core	SAMPLE TYPE	Description	Log	Additional Information
	2			WATER		
	4					
-5.7						River Bed
	6			Very soft grey silty clay		Insitu Vane Tests →
	8	D3/1				
	10					
	12	D3/2		Very soft grey silty clay with shells		
	14					
	16	D3/3		ditto more shells		
	18					
	20	D3/4		ditto		

Units: S.I.

Symbols:  75 mm ϕ U.D. Sample



DEPARTMENT OF PUBLIC WORKS TASMANIA
MATERIALS AND RESEARCH DIVISION

BORE LOG RECORD

PROJECT		SECOND HOBART CROSSING PHASE 1 - SITE INVESTIGATION		BORE No. D3	
Bore co-ordinates: 324754E 257307N				FILE No. 01.0500	
Surface R.L.: 0.00		Datum: State		Sheet no. 2 of 3	
Angle from horizontal: 90°		Direction: -			
Rig type: Meyhew 1000		Drill size: 6" Casing	Commenced: 21.4.76	Logged: T.S.	
Drilling by: Mines Dept.		Water level: River	Completed: 11.5.76	Checked: W.K.	

R.L.	Depth	Sample Core	SAMPLE TYPE	Description	Log	Additional Information
-23.07	22			Very soft grey silty clay with shells		
						U.D. sampling at -23 unsuccessful
	24			Continued on Drill Log Record Sheet 3		

Units: S.I.

Symbols:

