
Seismic Daily Report for 19 Mar 2008

Cue Energy Resources Ltd

Cue 2D

T 37_38P Bass Straight Australia

CGGVeritas: Pacific Titan

Contents

Daily Report for 19 Mar 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	1
Total Survey Hours	1
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	2
Activities	2
Comments	3
Plots	4

Daily Report for 19 Mar 2008

Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	03:39	3.650	SB	01	Continuation line VCUE08-E14-006, completed.
03:39	05:21	1.700	SB	02	Line change to VCUE08-E10-007.
05:21	11:27	6.100	SB	01	Commenced line VCUE08-E10-007, completed no problems encountered.
11:27	13:06	1.650	SB	02	Line change to line VCUE08-E06-008.
13:06	16:31	3.417	SB	01	Commenced line VCUE08-E06-008, completed.
16:31	18:41	2.167	SB	02	Line change to line VCUE08-E04-009.
18:41	22:09	3.467	SB	01	Commenced line VCUE08-E04-009, completed within specs.
22:09	23:52	1.717	SB	02	Line change to line VCUE08-E07-010.
23:52	24:00	0.133	SB	01	Commenced line VCUE08-E07-010, MSP 1051.

Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	16.767		16.767
02	Prime - Line Change	7.233		7.233
	Totals	24.00	0.00	24.00

Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
006	VCUE08-E14-006	357	1950	3333	34.60000	31.60000	34.60000
007	VCUE08-E10-007	177	3217	881	58.42500	55.42500	58.42500
008	VCUE08-E06-008	357	1001	2291	32.27500	29.27500	32.27500
009	VCUE08-E04-009	177	2177	881	32.42500	29.42500	32.42500
010	VCUE08-E07-010	357	1001	1051	1.27500	1.27500	1.27500

Total Daily Prime Production

KM	KMFF	CMP
159.00000	147.00000	159.00000

Line Comments

Seq	Line	Comments
006	VCUE08-E14-006	Recording line VCUE08-E14-006, completed start of line noise record a little high due to the tail end of the streamer snaking around, winds up to 30Kts with seas to 2m and a SW swell of 2m, the weather did improve throughout the line.
007	VCUE08-E10-007	Recording line VCUE08-E10-007, completed within specs.
008	VCUE08-E06-008	Recording line VCUE08-E06-008, completed within specs.
009	VCUE08-E04-009	Recording line VCUE08-E04-009, completed no problems.

Survey Totals

Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	50.983		50.983
02	Prime - Line Change	15.733		15.733
19	Transit from midpoint between Tap Oil & Cue Energy	1.283		1.283
	Totals	68.00	0.00	68.00

Total Survey Prime Production

KM	KMFF	CMP
474.67500	447.67500	474.67500

Percent Survey Completed by KMFF = 12.24%

Percentage Survey Completed by sail CMP = 11.89%

HSE

Exposure Hours

Type	19 Mar	Cumulative
client_hours	24	68
maritime_hours	384	1088
seismic_hours	408	1156
third_party_hours	24	68
Total	840	2380

Total man days: 99.1666666667

Incidents

Type	19 Mar	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

Comments

6 Toolbox meetings held at shift change.

1 Toolbox meeting held for source retrieval.

1 Toolbox meeting held for source deployment.


Activities

Type	19 Mar	Cumulative
Safety Drills	0	0
Safety Meetings	0	0
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	8	22
Helicopter Landings	0	0
Safety Audit - Internal	0	0
Safety Audit - External	0	0


Comments

Another good day's recording with lines VCUE08-E14,E10,E06 & E04 being completed and line E07 up to midnight. While recording line VCUE08-E04 a submarine surfaced off the starboard beam at a range of 6 miles, tried to contact the vessel on radio channel 16 as it was encroaching within safety area. When there was no reply 4 flares were fired and the ALDIS Light was used to attract attention, radio contact was eventually made and the submarine altered course giving the vessel a wide berth. Submarine plotted on radar until well clear of the vessel.

Plots

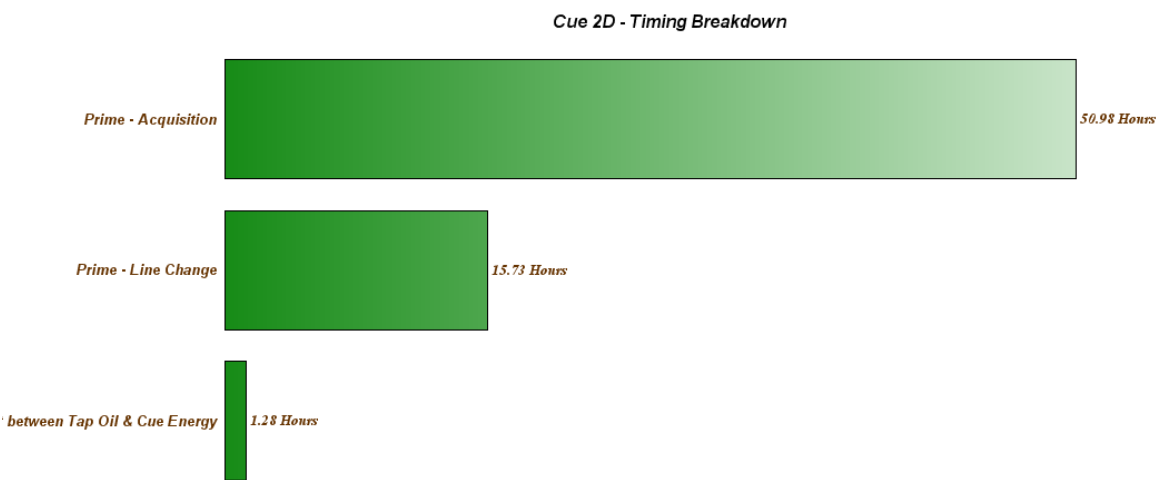

created with ChartDirector from www.advsofteng.com

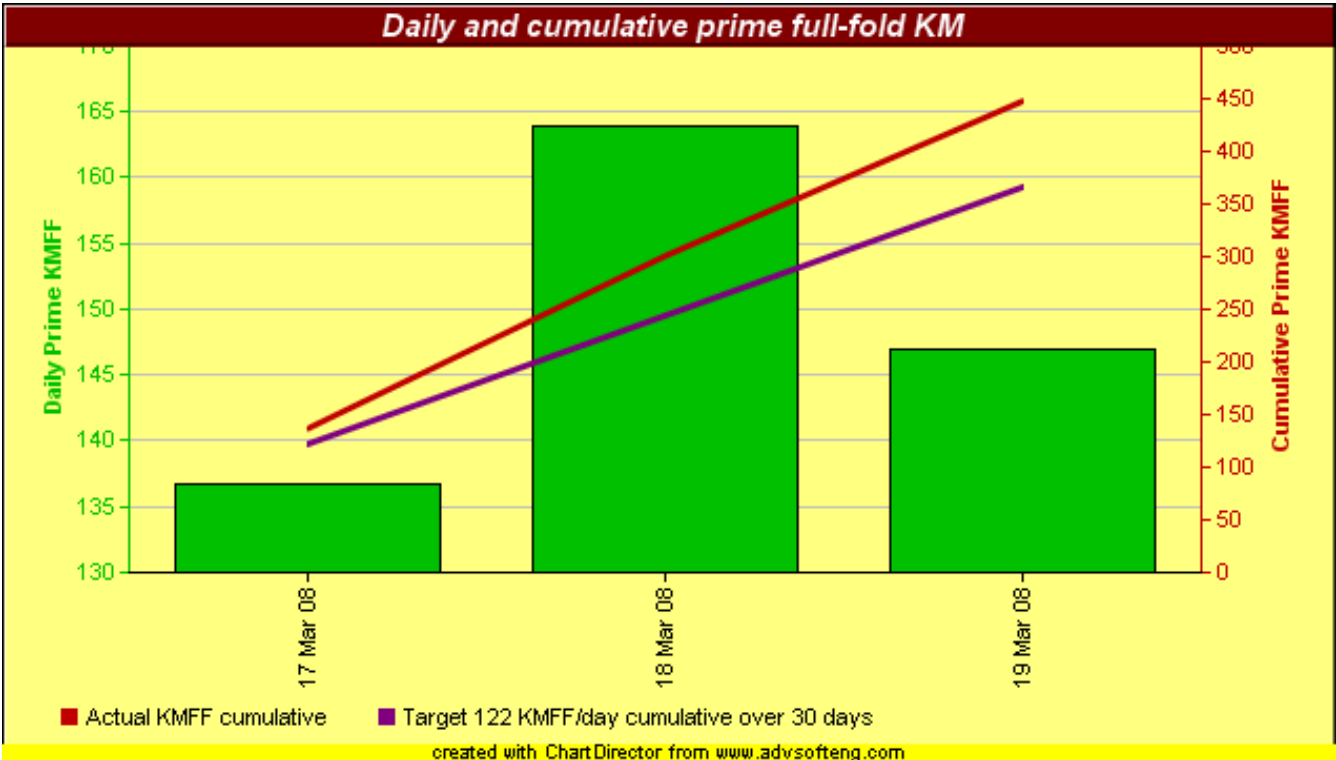

created with ChartDirector from www.advsofteng.com
