

---

Seismic Daily Report for 06 Apr 2008

Cue Energy Resources Ltd

Cue 2D

T 37\_38P Bass Straight Australia

CGGVeritas: Pacific Titan

---

# Contents

Daily Report for 06 Apr 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	1
Total Survey Hours	1
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	2
Activities	2
Comments	3
Plots	4

---

# Daily Report for 06 Apr 2008

## Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	02:08	2.133	SB	01	Continuation line VCUE08-N19-067, completed within spec.
01:08	03:45	2.617	SB	02	Line change to line VCUE08-N14-068. There is one extra hour added in due to the end of daylight saving.
03:45	09:35	5.833	SB	01	Commenced line VCUE08-N14-068, completed within specs.
09:35	11:15	1.667	SB	02	Line change to line VCUE08-N18-069.
11:15	16:34	5.317	SB	01	Commenced line VCUE08-N18-069, completed within spec.
16:34	18:15	1.683	SB	02	Line change to line VCUE08-N13-070.
18:15	24:00	5.750	SB	01	Commenced line VCUE08-N13-070, MSP 3075

## Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	19.033		19.033
02	Prime - Line Change	5.967		5.967
	Totals	25.00	0.00	25.00

## Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
067	VCUE08-N19-067	267	2116	881	30.90000	27.90000	30.90000
068	VCUE08-N14-068	087	1001	3188	54.70000	51.70000	54.70000
069	VCUE08-N18-069	267	2864	881	49.60000	46.60000	49.60000
070	VCUE08-N13-070	087	1001	3075	51.87500	51.87500	51.87500

## Total Daily Prime Production

KM	KMFF	CMP
187.07500	178.07500	187.07500

## Line Comments

Seq	Line	Comments
067	VCUE08-N19-067	Recording line VCUE08-N19-067, completed within spec.
068	VCUE08-N14-068	Recording line VCUE08-N14-068, completed within spec.
069	VCUE08-N18-069	Recording line VCUE08-N18-069, completed within spec.

## Survey Totals

### Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	242.233		242.233
02	Prime - Line Change	119.500		119.500
09	Shared Weather Down Time.	66.000		66.000
10	Weather	20.000		20.000

Code	Comment	Client Time	Contractor Time	Duration
19	Transit from midpoint between Tap Oil & Cue Energy	1.283		1.283
29	Operator error		2.833	2.833
30	Source		4.233	4.233
31	Compressors		3.067	3.067
54	Scheduled Port Call/Resupply		41.850	41.850
	Totals	449.02	51.98	501.00

## Total Survey Prime Production

KM	KMFF	CMP
2266.00000	2067.80000	2266.00000

Percent Survey Completed by KMFF = 56.52%

Percentage Survey Completed by sail CMP = 56.77%

## HSE

### Exposure Hours

Type	06 Apr	Cumulative
client_hours	24	500
maritime_hours	384	8000
seismic_hours	384	8404
third_party_hours	24	500
Total	816	17404

Total man days: 725.166666667

### Incidents

Type	06 Apr	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

### Comments

6 Toolbox meetings held at shift change.

### Activities


---

Type	06 Apr	Cumulative
Safety Drills	0	3
Safety Meetings	0	1
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	6	147
Helicopter Landings	0	0
Safety Audit - Internal	0	1
Safety Audit - External	0	0


## Comments

Very good days production with lines VCUE08-N19, N14 & N18 completed and line N13 until midnight. There is an extra hour in the daily log due to the end of daylight saving.

# Plots

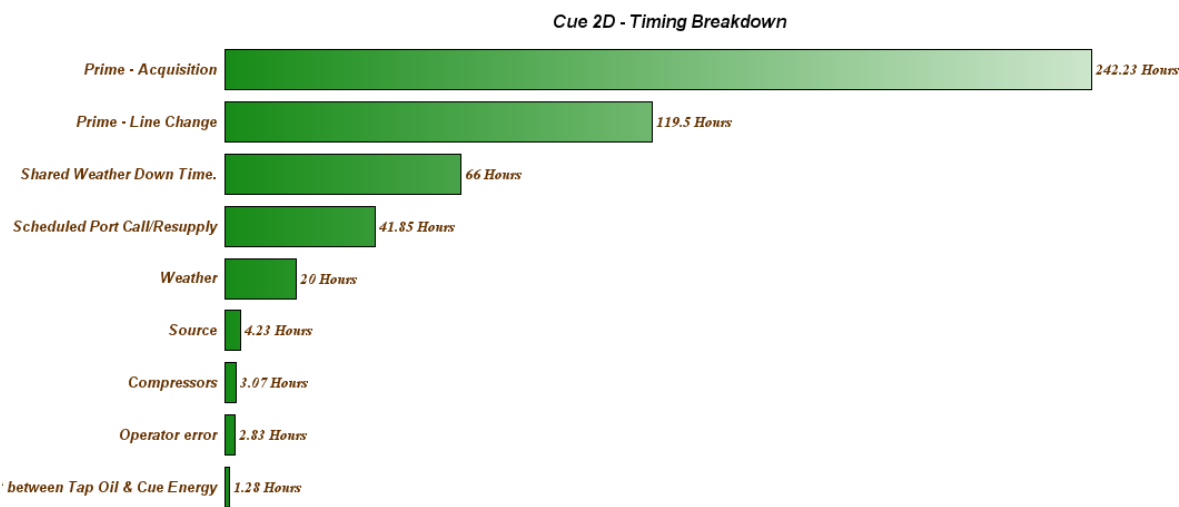

created with ChartDirector from [www.advsofteng.com](http://www.advsofteng.com)

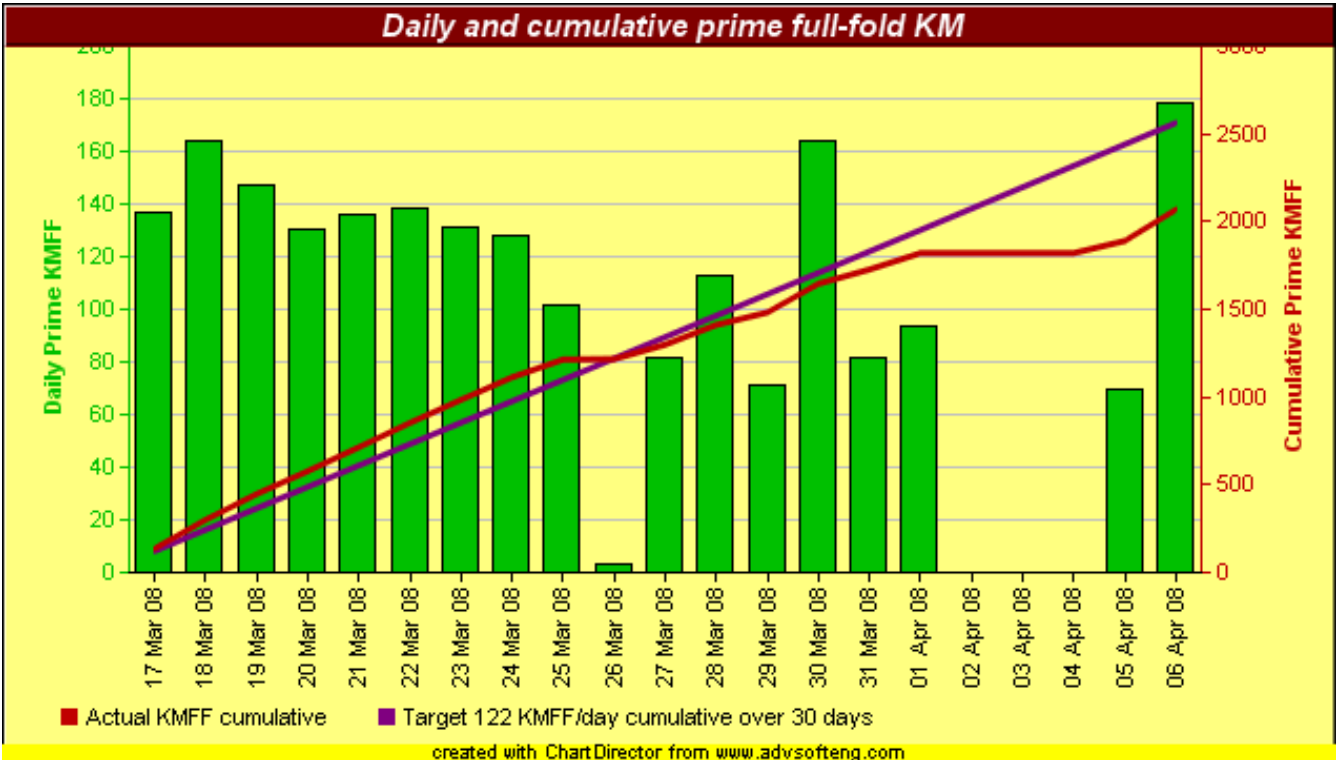

created with ChartDirector from [www.advsofteng.com](http://www.advsofteng.com)
