
Seismic Daily Report for 10 Apr 2008

Cue Energy Resources Ltd

Cue 2D

T 37_38P Bass Straight Australia

CGGVeritas: Pacific Titan

Contents

Daily Report for 10 Apr 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	1
Total Survey Hours	1
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	2
Activities	3
Comments	3
Plots	4

Daily Report for 10 Apr 2008

Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	02:40	2.667	SB	01	Continuation line VCUE08-N04-080, completed no raw GPS data to P2 files from SP 2921-2885.
02:40	04:21	1.683	SB	02	Line change to line VCUE08-N08-081.
04:21	10:39	6.300	SB	01	Commenced line VCUE08-N08-081, completed within spec.
10:39	12:16	1.617	SB	02	Line change to line VCUE08-N03-082.
12:16	18:24	6.133	SB	01	Commenced line VCUE08-N03-082, completed within spec.
18:24	20:21	1.950	SB	02	Line change to line VCUE08-N07-083.
20:21	24:00	3.650	SB	01	Commenced line VCUE08-N07-083, MSP 2309.

Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	18.750		18.750
02	Prime - Line Change	5.250		5.250
	Totals	24.00	0.00	24.00

Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
080	VCUE08-N04-080	267	1903	881	25.57500	22.57500	25.57500
081	VCUE08-N08-081	087	1001	3291	57.27500	54.27500	57.27500
082	VCUE08-N03-082	267	3166	881	57.15000	54.15000	57.15000
083	VCUE08-N07-083	087	1001	2309	32.72500	32.72500	32.72500

Total Daily Prime Production

KM	KMFF	CMP
172.72500	163.72500	172.72500

Line Comments

Seq	Line	Comments
080	VCUE08-N04-080	Recording line VCUE08-N04-080, completed, lost raw logging of GPS data from SPM2 on P2 from SP 2918-2889 still recording positions using SPM1 without any raw data output.
081	VCUE08-N08-081	Recording line VCUE08-N08-081, completed within spec.

Survey Totals

Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	313.083		313.083
02	Prime - Line Change	142.400		142.400
09	Shared Weather Down Time.	77.000		77.000
10	Weather	12.000		12.000

Code	Comment	Client Time	Contractor Time	Duration
19	Transit from midpoint between Tap Oil & Cue Energy	1.283		1.283
25	Port call		13.250	13.250
26	Travel		15.333	15.333
27	Deployment/Retrieval		8.467	8.467
29	Operator error		2.833	2.833
30	Source		8.283	8.283
31	Compressors		3.067	3.067
	Totals	545.77	51.23	597.00

Total Survey Prime Production

KM	KMFF	CMP
2917.12500	2682.92500	2917.12500

Percent Survey Completed by KMFF = 73.33%

Percentage Survey Completed by sail CMP = 73.08%

HSE

Exposure Hours

Type	10 Apr	Cumulative
client_hours	24	596
maritime_hours	384	9536
seismic_hours	384	9940
third_party_hours	24	596
Total	816	20668

Total man days: 861.166666667

Incidents

Type	10 Apr	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

Comments

6 Toolbox meetings at shift change.

-
- 1 Toolbox meeting for source retrieval.
 - 1 Toolbox meeting for source deployment.


Activities

Type	10 Apr	Cumulative
Safety Drills	1	4
Safety Meetings	0	1
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	8	177
Helicopter Landings	0	0
Safety Audit - Internal	0	1
Safety Audit - External	0	0


Comments

Good day's production with lines VCUE08-N04,N08 & N03 completed and line N07 up to midnight.

Plots

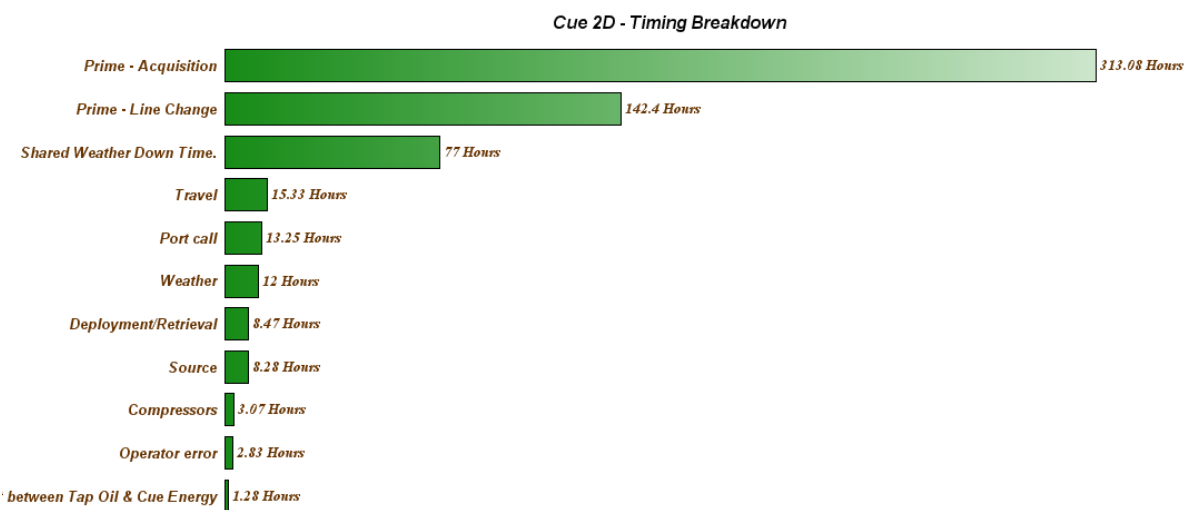

created with ChartDirector from www.advsofteng.com

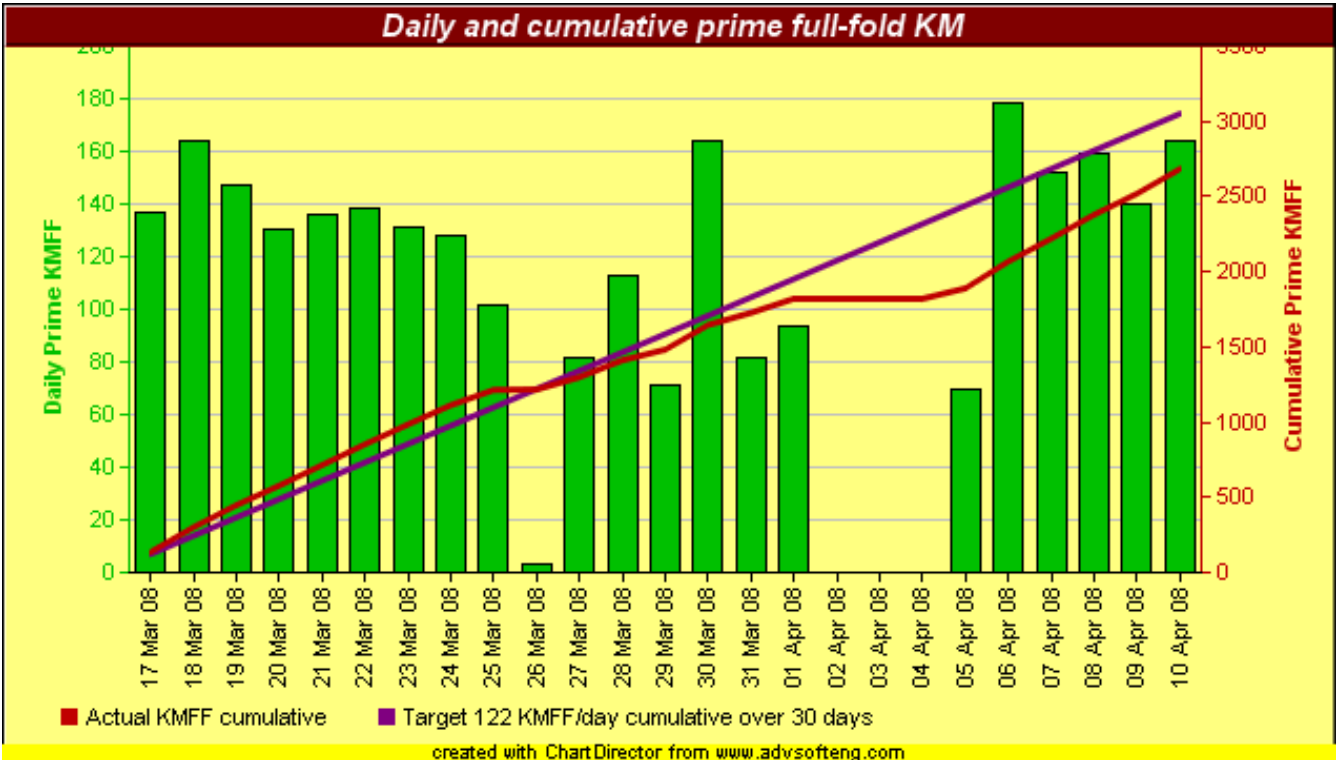

created with ChartDirector from www.advsofteng.com
