
Seismic Daily Report for 12 Apr 2008

Cue Energy Resources Ltd

Cue 2D

T 37_38P Bass Straight Australia

CGGVeritas: Pacific Titan

Contents

| | |
|---------------------------------|---|
| Daily Report for 12 Apr 2008 | 1 |
| Daily Time and Activity Summary | 1 |
| Daily Timing | 1 |
| Prime Production | 1 |
| Total Daily Prime Production | 1 |
| Line Comments | 1 |
| Survey Totals | 1 |
| Total Survey Hours | 1 |
| Total Survey Prime Production | 2 |
| HSE | 2 |
| Exposure Hours | 2 |
| Incidents | 2 |
| Activities | 3 |
| Comments | 3 |
| Plots | 4 |

Daily Report for 12 Apr 2008

Daily Time and Activity Summary

| Start | End | Duration | Category | Code | Comment |
|-------|-------|----------|----------|------|--|
| 00:00 | 02:40 | 2.667 | SB | 01 | Continuation line VCUE08-N01-086, completed within spec. |
| 02:40 | 07:10 | 4.500 | SB | 02 | Line change to line VCUE08-E18-087. Vessel position V1G3 (Multifix position) changed from antenna offsets now running off SPM1. |
| 07:10 | 09:45 | 2.583 | SB | 01 | Commenced line VCUE08-E18-087, terminated early due to airleak LGSP 1985. No ionopheric data being recorded. Circling around to complete the line. |
| 09:45 | 13:44 | 3.983 | DT | 30 | Circling around back to line VCUE08-E18-088 due to an airleak. |
| 13:44 | 17:36 | 3.867 | SB | 01 | Commenced line VCUE08-E18-088, completed still not recording any ionopheric data. |
| 17:36 | 19:28 | 1.867 | SB | 02 | Line change to line VCUE08-E22-089. |
| 19:28 | 24:00 | 4.533 | SB | 01 | Commenced line VCUE08-E22-089, completed still not getting any ionopheric data. |

Daily Timing

| Code | Comment | Client Time | Contractor Time | Duration |
|------|---------------------|-------------|-----------------|----------|
| 01 | Prime - Acquisition | 13.650 | | 13.650 |
| 02 | Prime - Line Change | 6.367 | | 6.367 |
| 30 | Source | | 3.983 | 3.983 |
| | Totals | 20.02 | 3.98 | 24.00 |

Prime Production

| seq | line | dir | FCSP | LCSP | KM | KMFF | CMP |
|-----|----------------|-----|------|------|----------|----------|----------|
| 086 | VCUE08-N01-086 | 267 | 1856 | 881 | 24.40000 | 21.40000 | 24.40000 |
| 087 | VCUE08-E18-087 | 357 | 1001 | 1985 | 24.62500 | 24.62500 | 24.62500 |
| 088 | VCUE08-E18-088 | 357 | 1986 | 3333 | 33.70000 | 30.70000 | 33.70000 |
| 089 | VCUE08-E22-089 | 177 | 3213 | 1575 | 40.97500 | 40.97500 | 40.97500 |

Total Daily Prime Production

| KM | KMFF | CMP |
|-----------|-----------|-----------|
| 123.70000 | 117.70000 | 123.70000 |

Line Comments

| Seq | Line | Comments |
|-----|----------------|---|
| 086 | VCUE08-N01-086 | Recording line VCUE08-N01-086, MSP 1857. |
| 087 | VCUE08-E18-087 | Recording line VCUE08-E18-087, completed not receiving any ionopheric correction data. |
| 088 | VCUE08-E18-088 | Recording line VCUE08-E18-088, completed continuation of sequence 087 for airleak. Still no getting any ionopheric correction data. |

Survey Totals

Total Survey Hours

| Code | Comment | Client Time | Contractor Time | Duration |
|------|--|-------------|-----------------|----------|
| 01 | Prime - Acquisition | 345.717 | | 345.717 |
| 02 | Prime - Line Change | 153.783 | | 153.783 |
| 09 | Shared Weather Down Time. | 77.000 | | 77.000 |
| 10 | Weather | 12.000 | | 12.000 |
| 19 | Transit from midpoint between Tap Oil & Cue Energy | 1.283 | | 1.283 |
| 25 | Port call | | 13.250 | 13.250 |
| 26 | Travel | | 15.333 | 15.333 |
| 27 | Deployment/Retrieval | | 8.467 | 8.467 |
| 29 | Operator error | | 2.833 | 2.833 |
| 30 | Source | | 12.267 | 12.267 |
| 31 | Compressors | | 3.067 | 3.067 |
| | Totals | 589.78 | 55.22 | 645.00 |

Total Survey Prime Production

| KM | KMFF | CMP |
|------------|------------|------------|
| 3212.37500 | 2963.17500 | 3212.37500 |

Percent Survey Completed by KMFF = 80.99%

Percentage Survey Completed by sail CMP = 80.47%

HSE

Exposure Hours

| Type | 12 Apr | Cumulative |
|-------------------|--------|------------|
| client_hours | 24 | 644 |
| maritime_hours | 384 | 10304 |
| seismic_hours | 384 | 10708 |
| third_party_hours | 24 | 644 |
| Total | 816 | 22300 |

Total man days: 929.166666667

Incidents

| Type | 12 Apr | Cumulative |
|-------------------------------|--------|------------|
| Fatality | 0 | 0 |
| Lost Time Incident | 0 | 0 |
| Medical Treatment | 0 | 0 |
| First Aid | 0 | 0 |
| Restricted Work | 0 | 0 |
| Material Loss/Damage | 0 | 0 |
| Environmental Incident/Damage | 0 | 0 |
| Near Miss | 0 | 0 |
| Hazard | 0 | 0 |
| Unsafe Act | 0 | 0 |

| Type | 12 Apr | Cumulative |
|-------|--------|------------|
| Total | 0 | 0 |

Comments

6 Toolbox meetings held at shift change.

1 Toolbox meeting held for source retrieval.

1 Toolbox meeting held for source deployment.


Activities

| Type | 12 Apr | Cumulative |
|-------------------------|--------|------------|
| Safety Drills | 0 | 4 |
| Safety Meetings | 0 | 1 |
| Boat Launches | 0 | 0 |
| Boat Transfers | 0 | 0 |
| Toolbox Meetings | 8 | 193 |
| Helicopter Landings | 0 | 0 |
| Safety Audit - Internal | 0 | 1 |
| Safety Audit - External | 0 | 0 |


Comments

Production down today due to a longer than average line change and a circle on line VCUE08-E18 due to an airleak. Lines completed were VCUE08-N01,E18 and line E22 up to midnight. Vessel Position V1G3 (Multifix Position)changed antenna offsets now running of SPM1 this seem to have fixed the raw GPS data drop outs but it looks like the ionopheric data is missing.

Plots

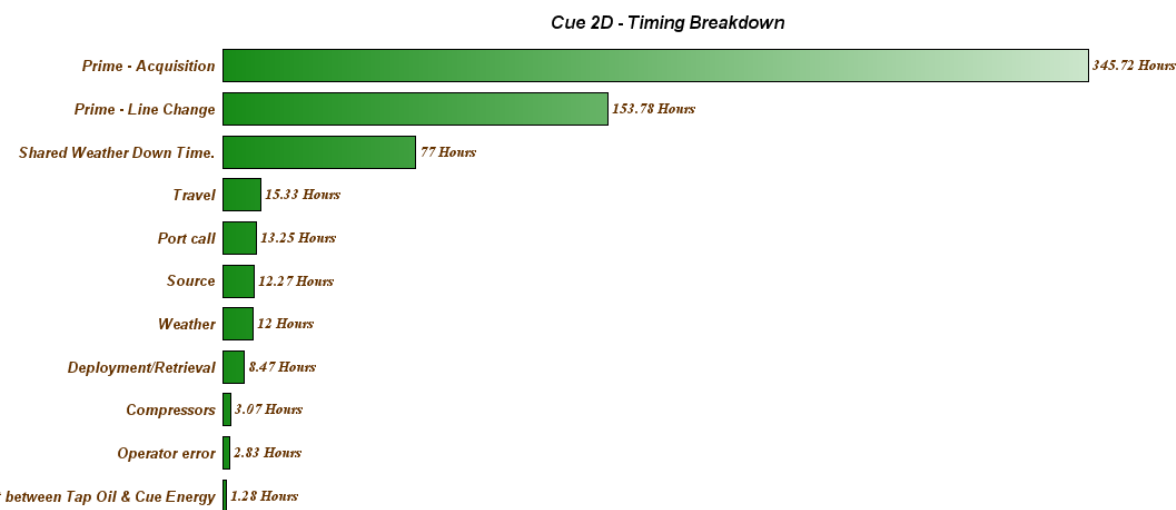

created with ChartDirector from www.advsofteng.com

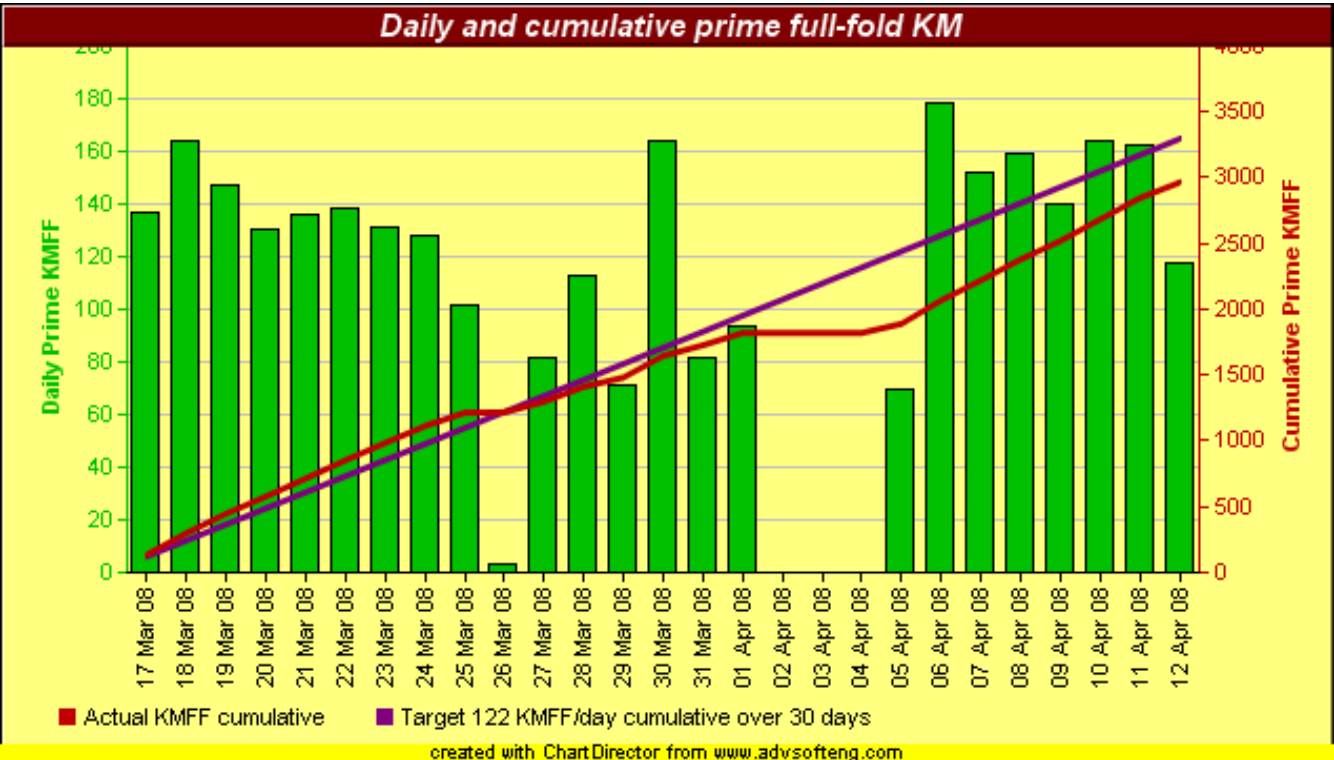

created with ChartDirector from www.advsofteng.com
