
Seismic Daily Report for 14 Apr 2008

Cue Energy Resources Ltd

Cue 2D

T 37_38P Bass Straight Australia

CGGVeritas: Pacific Titan

Contents

Daily Report for 14 Apr 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	2
Total Survey Hours	2
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	2
Activities	3
Comments	3
Plots	4

Daily Report for 14 Apr 2008

Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	01:07	1.117	SB	02	Line change from to line VCUE08-E32-093.
01:07	04:31	3.400	SB	01	Commenced line VCUE08-E32-093, completed within spec no ionopheric data recorded..
04:31	06:19	1.800	SB	02	Line change to line VCUE08-E37-094.
06:19	09:17	2.967	SB	01	Commenced line VCUE08-E37-094, completed within spec no ionopheric data recorded.
09:17	10:50	1.550	SB	02	Line change to line VCUE08-E41-095.
10:50	13:32	2.700	SB	01	Commenced line VCUE08-E41-095, completed within spec no ionopheric data recorded.
13:32	15:19	1.783	SB	02	Line change to line VCUE08-E35-096.
15:19	18:35	3.267	SB	01	Commenced line VCUE08-E35-096, completed within spec no ionopheric data recorded.
18:35	20:07	1.533	SB	02	Line change to line VCUE08-E39-097. Changed output of V1G3 from SPM1 to SPM2, new offsets for V1G3 entered into SPECTRA of antenna position.
20:07	22:56	2.817	SB	01	Commenced line VCUE08-E39-097, completed within spec.
22:56	24:00	1.067	SB	02	Line change to line VCUE08-E42-098.

Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	15.150		15.150
02	Prime - Line Change	8.850		8.850
	Totals	24.00	0.00	24.00

Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
093	VCUE08-E32-093	177	2235	881	33.87500	30.87500	33.87500
094	VCUE08-E37-094	357	1001	2094	27.35000	24.35000	27.35000
095	VCUE08-E41-095	177	1852	881	24.30000	21.30000	24.30000
096	VCUE08-E35-096	357	1001	2149	28.72500	27.30000	28.72500
097	VCUE08-E39-097	177	1897	881	25.42500	22.42500	25.42500

Total Daily Prime Production

KM	KMFF	CMP
139.67500	126.25000	139.67500

Line Comments

Seq	Line	Comments
093	VCUE08-E32-093	Recording line VCUE08-E32-093, completed within spec no ionopheric data being recorded.
094	VCUE08-E37-094	Recording line VCUE08-E37-094, completed within spec no ionopheric data being recorded. Some ships noise was evident at the front of the streamer between SP1753 to SP1766.
095	VCUE08-E41-095	Recording line VCUE08-E41-095, completed within spec no ionopheric data being recorded.

Seq	Line	Comments
096	VCUE08-E35-096	Recording line VCUE08-E35-096, completed within spec no ionopheric data being recorded.
097	VCUE08-E39-097	Recording line VCUE08-E39-097, completed within spec. On the previous line change the output of V1G3 was changed from SPM1 to SPM2, new offsets for antenna were entered into SPECTRA was X=5.25, Y=0.0 now X=4.20 Y=1.05.

Survey Totals

Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	379.033		379.033
02	Prime - Line Change	166.750		166.750
04	Infill - Line Change	1.717		1.717
09	Shared Weather Down Time.	77.000		77.000
10	Weather	12.000		12.000
19	Transit from midpoint between Tap Oil & Cue Energy	1.283		1.283
25	Port call		13.250	13.250
26	Travel		15.333	15.333
27	Deployment/Retrieval		8.467	8.467
29	Operator error		2.833	2.833
30	Source		12.267	12.267
31	Compressors		3.067	3.067
	Totals	637.78	55.22	693.00

Total Survey Prime Production

KM	KMFF	CMP
3519.97500	3245.35000	3519.97500

Percent Survey Completed by KMFF = 88.70%

Percentage Survey Completed by sail CMP = 88.18%

HSE

Exposure Hours

Type	14 Apr	Cumulative
client_hours	24	692
maritime_hours	384	11072
seismic_hours	384	11476
third_party_hours	24	692
Total	816	23932

Total man days: 997.166666667

Incidents

Type	14 Apr	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

Comments

6 Toolbox meetings held at shift change.


Activities

Type	14 Apr	Cumulative
Safety Drills	0	4
Safety Meetings	0	1
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	6	207
Helicopter Landings	0	0
Safety Audit - Internal	0	1
Safety Audit - External	0	0


Comments

Very good day's production with lines VCUE08-E32,E37,E41,E35 & E39 being completed. On the line change after line E35 changed the output of V1G3 from SPM1 to SPM2. new offsets for antenna for V1G3 entered into SPECTRA was X=5.25 Y=0.00 now X=4.20 Y=1.05.

Plots

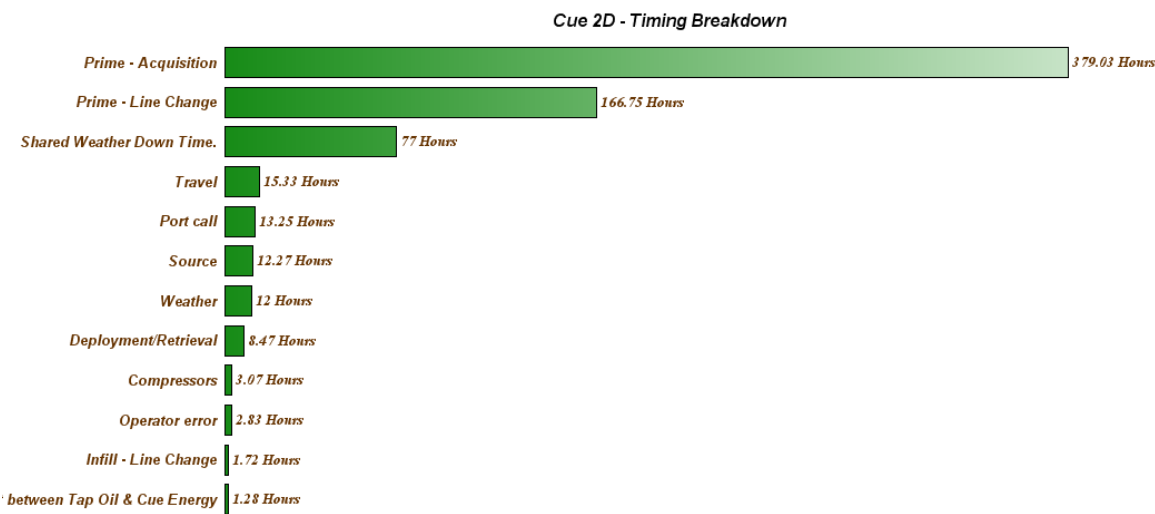

created with ChartDirector from www.advsofteng.com

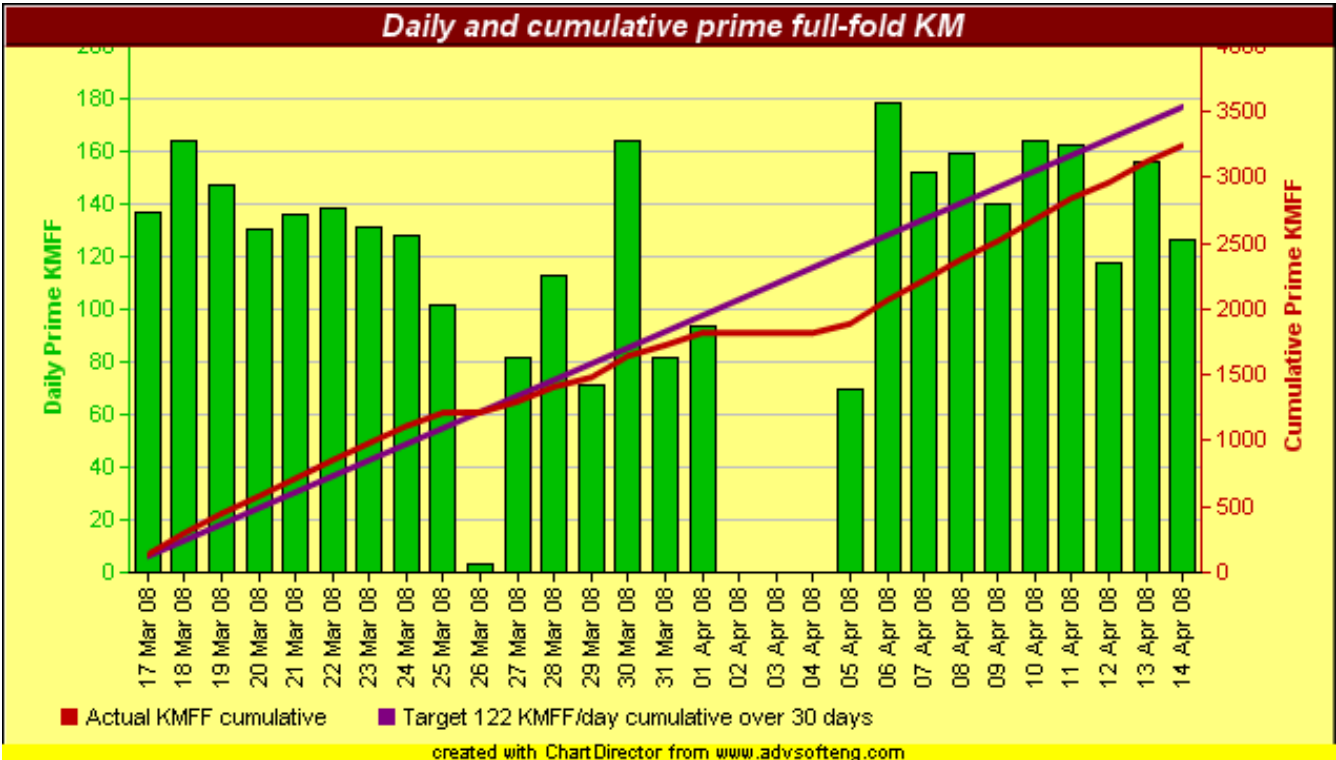

created with ChartDirector from www.advsofteng.com
