
Seismic Daily Report for 16 Apr 2008

Cue Energy Resources Ltd

Cue 2D

T 37_38P Bass Straight Australia

CGGVeritas: Pacific Titan

Contents

Daily Report for 16 Apr 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	2
Total Survey Hours	2
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	3
Activities	3
Comments	3
Plots	4

Daily Report for 16 Apr 2008

Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	01:09	1.150	SB	01	Continuation line VCUE08-E47-104, MSP 1370 compass S1C20 knocked out in SPECTRA due to high bias.
01:09	02:38	1.483	SB	02	Line change to line VCUE08-E51-105.
02:38	04:26	1.800	SB	01	Commenced line VCUE08-E51-105, completed within spec compass S1C20 out of SPECTRA due to high bias.
04:26	06:22	1.933	SB	02	Line change to line VCUE08-E43-106.
06:22	08:54	2.533	SB	01	Commenced line VCUE08-E43-106, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
08:54	10:49	1.917	SB	02	Line change to line VCUE08-E40-107.
10:49	13:37	2.800	SB	01	Commenced line VCUE08-E40-107, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
13:37	15:35	1.967	SB	02	Line change to line VCUE08-E34-108.
15:35	18:59	3.400	SB	01	Commenced line VCUE08-E34-108, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
18:59	20:35	1.600	SB	02	Line change to line VCUE08-E38-109.
20:35	22:37	2.033	SB	01	Commenced line VCUE08-E38-109, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
22:37	24:00	1.383	SB	02	Line change to line VCUE08-E33-110.

Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	13.717		13.717
02	Prime - Line Change	10.283		10.283
	Totals	24.00	0.00	24.00

Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
104	line VCUE08-E47	357	1371	1789	10.47500	7.47500	10.47500
105	VCUE08-E51-105	177	1550	881	16.75000	13.75000	16.75000
106	VCUE08-E43-106	357	1001	1901	22.52500	19.52500	22.52500
107	VCUE08-E40-107	177	1866	881	24.65000	21.65000	24.65000
108	VCUE08-E34-108	357	1001	2191	29.77500	26.77500	29.77500
109	VCUE08-E38-109	177	1942	881	26.55000	23.55000	26.55000

Total Daily Prime Production

KM	KMFF	CMP
130.72500	112.72500	130.72500

Line Comments

Seq	Line	Comments
104	line VCUE08-E47	Recording line VCUE08-E47-104, MSP 1370 compass S1C20 knocked out in SPECTRA due to high bias. At SOL some low level ships noise from ahead of the vessel and from SP 1095 - 1265 ships noise abeam of the vessel.
105	VCUE08-E51-105	Recording line VCUE08-E51-105, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
106	VCUE08-E43-106	Recording line VCUE08-E43-106, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
107	VCUE08-E40-107	Recording line VCUE08-E40-107, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
108	VCUE08-E34-108	Recording line VCUE08-E34-109, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
109	VCUE08-E38-109	Recording line VCUE08-E38-109, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.

Survey Totals

Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	407.000		407.000
02	Prime - Line Change	186.783		186.783
04	Infill - Line Change	1.717		1.717
09	Shared Weather Down Time.	77.000		77.000
10	Weather	12.000		12.000
19	Transit from midpoint between Tap Oil & Cue Energy	1.283		1.283
25	Port call		13.250	13.250
26	Travel		15.333	15.333
27	Deployment/Retrieval		8.467	8.467
29	Operator error		2.833	2.833
30	Source		12.267	12.267
31	Compressors		3.067	3.067
	Totals	685.78	55.22	741.00

Total Survey Prime Production

KM	KMFF	CMP
3771.50000	3460.87500	3771.50000

Percent Survey Completed by KMFF = 94.59%

Percentage Survey Completed by sail CMP = 94.48%

HSE

Exposure Hours

Type	16 Apr	Cumulative
client_hours	24	740
maritime_hours	384	11840
seismic_hours	384	12244

Type	16 Apr	Cumulative
third_party_hours	24	740
Total	816	25564

Total man days: 1065.16666667

Incidents

Type	16 Apr	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

Comments

6 Toolbox meetings at shift change.

1 Toolbox meeting held for source retrieval.

1 Toolbox meeting held for source deployment.


Activities

Type	16 Apr	Cumulative
Safety Drills	0	4
Safety Meetings	0	1
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	8	223
Helicopter Landings	0	0
Safety Audit - Internal	0	1
Safety Audit - External	0	0


Comments

Another good day's production with lines VCUE08-E47, E51, E43, E40, E34 & E38 completed.

Plots

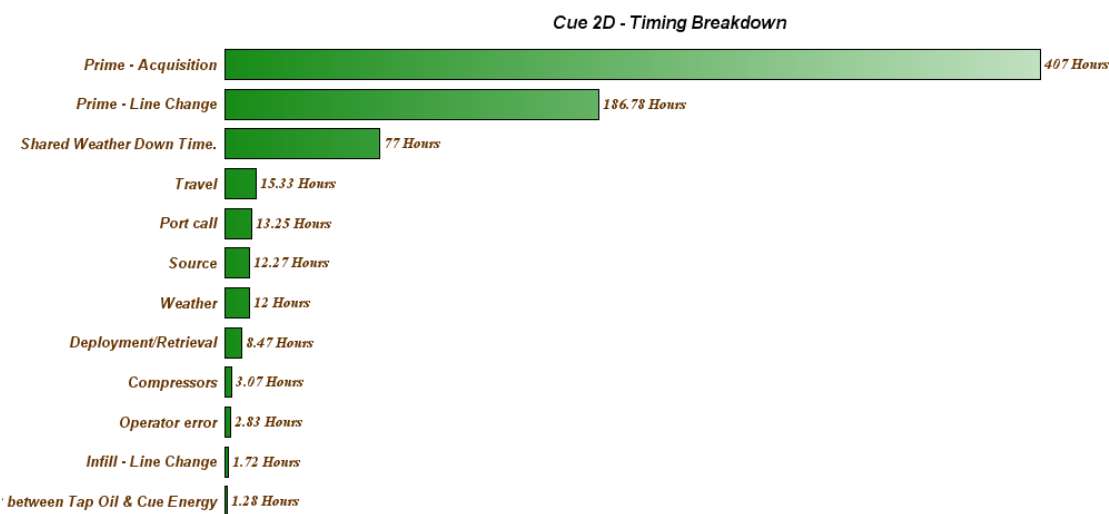

created with ChartDirector from www.advsofteng.com

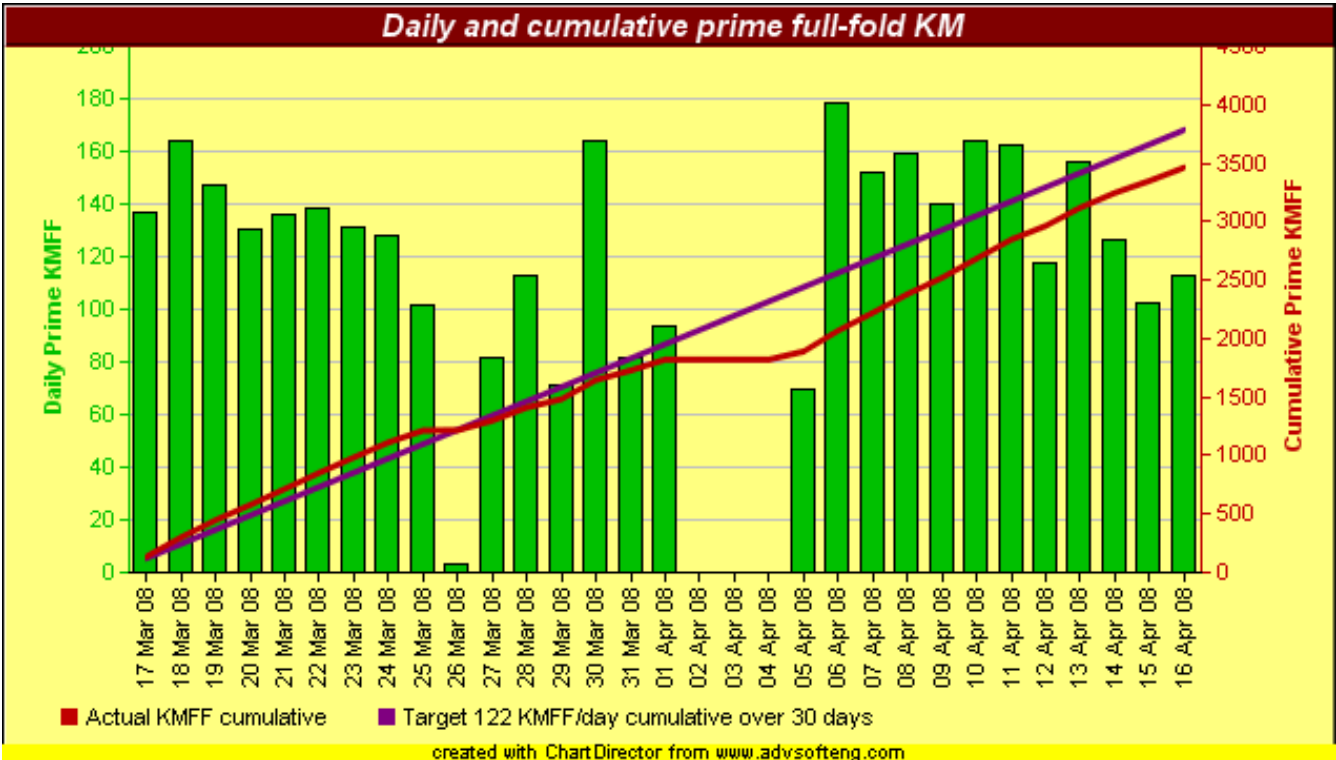

created with ChartDirector from www.advsofteng.com
