

---

Seismic Daily Report for 04 May 2008

3D Oil

3D Oil T41P 2D

T41P Bass Straight Australia

CGGVeritas: Pacific Titan

---

# Contents

Daily Report for 04 May 2008	1
Daily Time and Activity Summary	1
Daily Timing	1
Prime Production	1
Total Daily Prime Production	1
Line Comments	1
Survey Totals	1
Total Survey Hours	1
Total Survey Prime Production	2
HSE	2
Exposure Hours	2
Incidents	2
Activities	2
Comments	3
Plots	4

---

# Daily Report for 04 May 2008

## Daily Time and Activity Summary

Start	End	Duration	Category	Code	Comment
00:00	08:06	8.100	SB	01	Continuation of line TDOB08-025-068, completed within spec compass S1C20 knocked out in SPECTRA due to high bias.
08:06	09:48	1.700	SB	02	Line change to line TDOB08-021-069
09:48	17:10	7.367	SB	01	Commenced line TDOB08-021-069, completed within spec compass S1C20 knocked out in SPECTRA due to high bias. This completes the lines in the 3D Oil survey
17:10	18:40	1.500	SB	19	Mid way point between 3D Oil and Bass Strait surveys at 18:40 position 040°12'11S 147°12'24E this completes the 3D Oil Survey.

## Daily Timing

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	15.467		15.467
02	Prime - Line Change	1.700		1.700
19	Transit from midpoint between 3D Oil & Bass Strait	1.500		1.500
	Totals	18.67	0.00	18.67

## Prime Production

seq	line	dir	FCSP	LCSP	KM	KMFF	CMP
068	TDOB08-025-068	307	1069	3887	70.47500	67.47500	70.47500
069	TDOB08-021-069	133	3739	1001	68.47500	65.47500	68.47500

## Total Daily Prime Production

KM	KMFF	CMP
138.95000	132.95000	138.95000

## Line Comments

Seq	Line	Comments
068	TDOB08-025-068	Recording line TDOB08-025-068, completed within spec compass S1C20 knocked out in SPECTRA due to high bias. Several false autofires logged these were checked by the Seis QC and found to be false the sensor line to gun 3-7 was disabled. At the end of the line the noise strip was high due to a vessel passing abeam of us.
069	TDOB08-021-069	Recording line TDOB08-021-069, MSP 1068 compass S1C20 knocked out in SPECTRA due to high bias.

## Survey Totals

### Total Survey Hours

Code	Comment	Client Time	Contractor Time	Duration
01	Prime - Acquisition	243.817		243.817
02	Prime - Line Change	120.667		120.667

Code	Comment	Client Time	Contractor Time	Duration
19	Transit from midpoint between 3D Oil & Bass Strait	4.250		4.250
30	Source		8.667	8.667
35	Instruments		7.233	7.233
38	Towing		3.033	3.033
	Totals	368.73	18.93	387.67

## Total Survey Prime Production

KM	KMFF	CMP
2219.27500	2021.30000	2219.27500

Percent Survey Completed by KMFF = 100.66%

Percentage Survey Completed by sail CMP = 100.74%

## HSE

### Exposure Hours

Type	04 May	Cumulative
client_hours	24	408
maritime_hours	384	6528
seismic_hours	384	6528
third_party_hours	24	408
Total	816	13872

Total man days: 578

### Incidents

Type	04 May	Cumulative
Fatality	0	0
Lost Time Incident	0	0
Medical Treatment	0	0
First Aid	0	0
Restricted Work	0	0
Material Loss/Damage	0	0
Environmental Incident/Damage	0	0
Near Miss	0	0
Hazard	0	0
Unsafe Act	0	0
Total	0	0

#### Comments

6 Toolbox meetings at shift change.

1 Toolbox meeting for source retrieval.

1 Toolbox meeting for source deployment.

### Activities


---

Type	04 May	Cumulative
Safety Drills	0	2
Safety Meetings	0	0
Boat Launches	0	0
Boat Transfers	0	0
Toolbox Meetings	8	117
Helicopter Landings	0	0
Safety Audit - Internal	0	0
Safety Audit - External	0	0


## Comments

Lines TDOB08-025 & 021 completed this completes the lines in the 3D Oil survey. Mid way point between 3D Oil and Bass Strait surveys at 18:40 position 040°12'11S 147°12'24E, this completes the 3D Oil Survey.

Plots

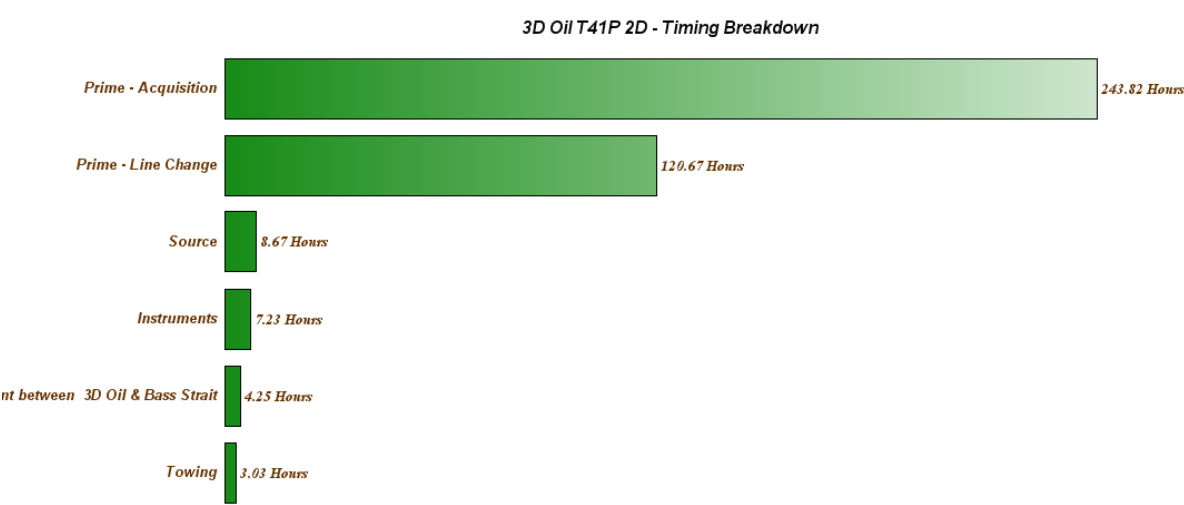

created with ChartDirector from [www.advsofteng.com](http://www.advsofteng.com)

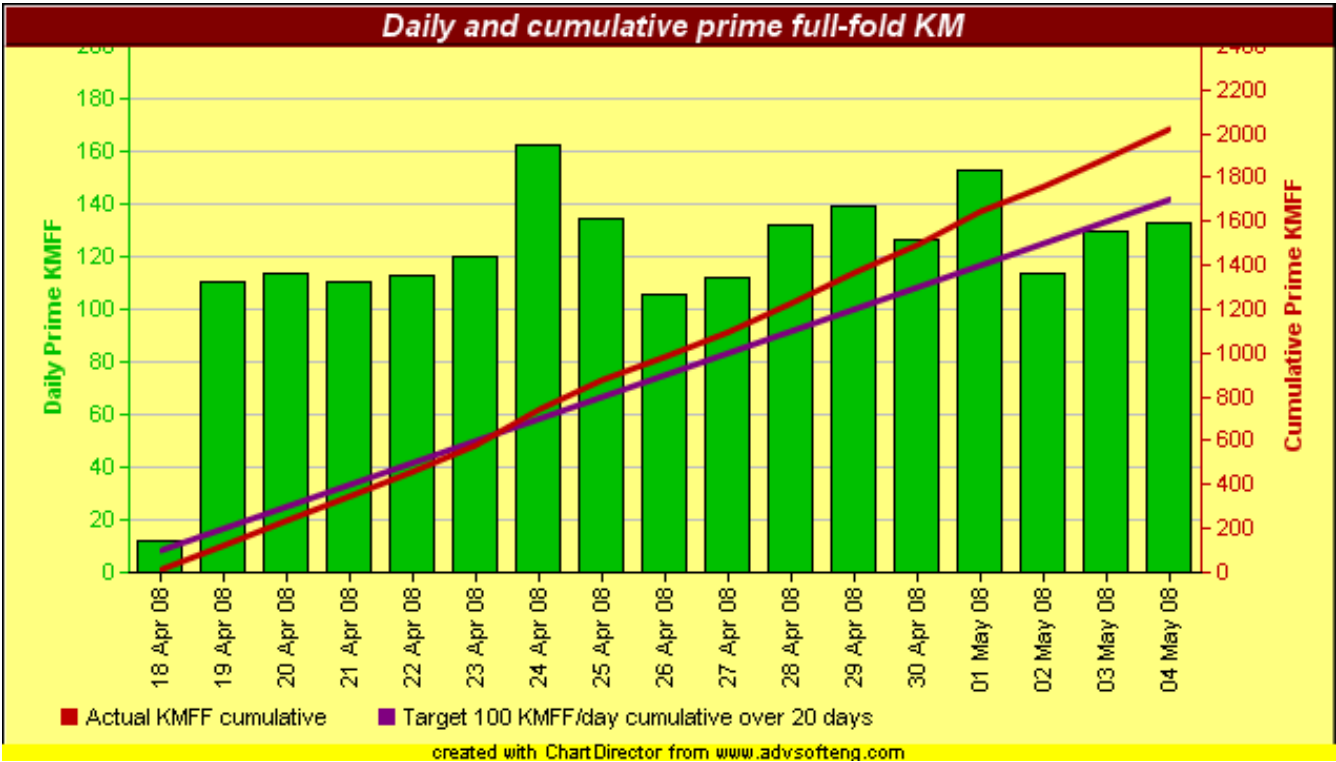

created with ChartDirector from [www.advsofteng.com](http://www.advsofteng.com)
